


Project: Thermalised rack installat	Task	Milestone	Project Summary	External Milestone	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	Deadline
Date: Thu 25/07/13	Split	Summary	External Tasks	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	Progress



ID	% Compl	Task Name	Duration	Start	Finish	Resource Names	Qtr 2, 2013			Qtr 3, 2013			Qtr 4, 2013			Qtr 1, 2014			Qtr 2, 2014			Qtr 3, 2014	
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
101	0%	SX4: Install Ethernet hubs and cables	1 day	Tue 03/12/13	Tue 03/12/13	IT/CS																	
102	0%	SX4: Install cable trays for optical fibers	1 day	Wed 04/12/13	Wed 04/12/13	BE/BI																	
103	0%	SX4: Install VME crates	1 day	Thu 05/12/13	Thu 05/12/13	BE/BI																	
104	0%	SX4: Install air deflectors and rack front panels	1 day	Fri 06/12/13	Fri 06/12/13	BE/BI																	
105	0%	SX4: Connect optical fibers	4 days	Mon 09/12/13	Thu 12/12/13	BE/BI																	
106	0%	SX4: Install water cooling pipes	15 days	Wed 04/12/13	Fri 10/01/14	EN/CV																	
107	0%	SX4: Test BPM and BLM acquisition chain	20 days	Fri 13/12/13	Tue 28/01/14	BE/BI																	
60	0%	Sector 3-4: RF ball test #2	1 day	Mon 31/03/14	Mon 31/03/14	TE/VSC																	
61	0%	Sector 4-5: RF ball test #2	1 day	Wed 30/04/14	Wed 30/04/14	TE/VSC																	
159	0%	Sector 3-4: BLM radiation test	3 days	Fri 20/06/14	Tue 24/06/14	BE/BI																	
160	0%	Sector 4-5: BLM radiation test	3 days	Fri 01/08/14	Tue 05/08/14	BE/BI																	
108	0%	P4: UPS works	48 days	Mon 03/03/14	Wed 07/05/14	EN/EL2																	
109	0%	Arc 34: UPS works	42 days	Mon 28/04/14	Tue 24/06/14	EN/EL2																	
110	0%	Arc 45: UPS R2E works (no power)	35 days	Mon 12/05/14	Fri 27/06/14	EN/EL2																	

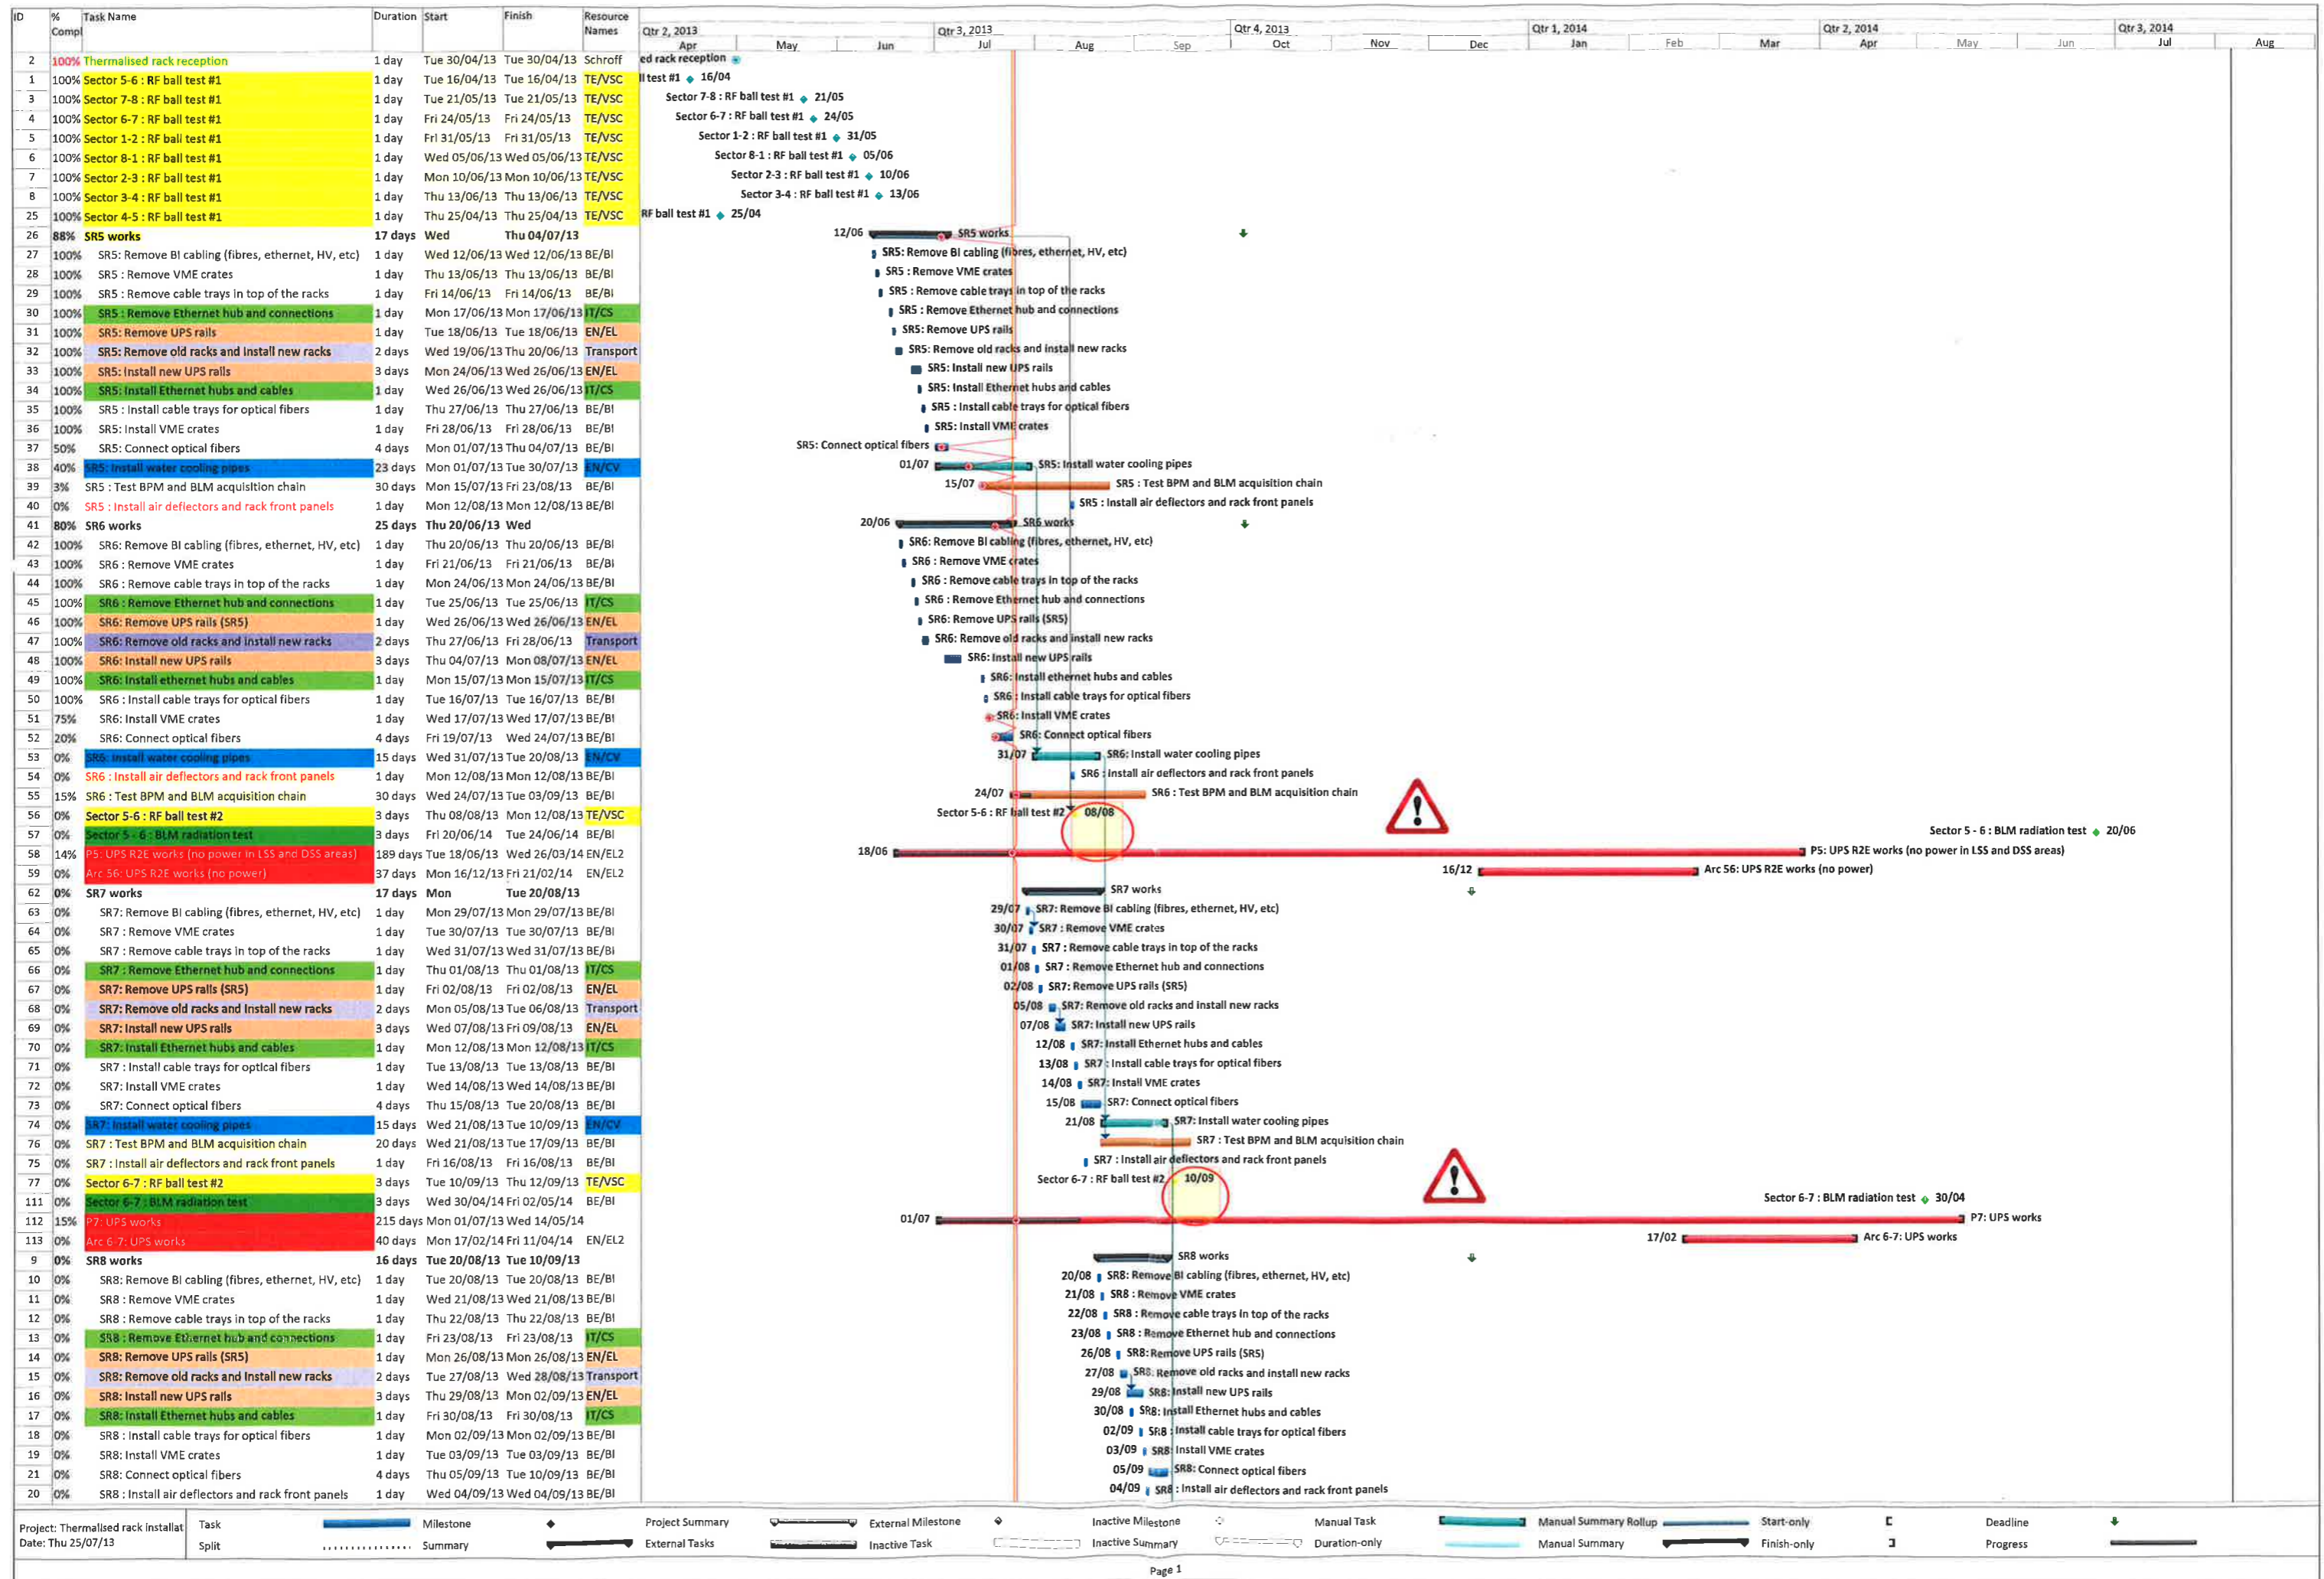
